DEP Form FD 9000-3 Physical/Chemical Characterization Field Sheet

SAMPLE ID: Peace River Homeland | ORG ID: | LATITUDE: 27.8193278
COUNTY: Polk | STORET #: | LONGITUDE: -81.7983762
DATE: 4/30/26 | TIME: 10:00 | SAMPLING AGENCY: USF&WL
SITE NAME: Peace River Homeland
FIELD ID/NAME: Peace River Homeland | RECEIVING BODY OF WATER: CHARLOTTE HARBOR

RIPARIAN ZONE / STREAM FEATURES

PREDOMINANT LAND-USE IN WATERSHED (specify relative percent in each category): Reclaimed Land

Forest/Natural	Silviculture	Field/Pasture	Agricultural	Residential	Commercial	Industry	Other (Specify)
72.53		0.93%		0.36%			24.05

Landscape Development Intensity Index (LDI): 2.88

Local Watershed Erosion (select one): ☐ None ☐ Slight ☑ Moderate ☐ Heavy

Local Watershed NPS Pollution: ☐ No evidence ☐ Slight ☑ Moderate ☐ Heavy

Width of Riparian Vegetation (m) on Each Buffer Side
Left Bank: >18 | Right Bank: >18

Hydrologic Modification Score (per FT 3101): 5

High Water Mark: 2.1 (m) + 0.35 (above present water level) = 2.45 (present depth) (above bed)

Artificially Impounded: ☐ Yes ☑ No

Typical Width (m) Depth (m)/Velocity (m/sec) Transect

10.7 m wide		
0.07 m/s	0.08 m/s	0.07 m/s
0.1 m deep	0.35 m deep	0.1 m deep

Artificially Channelized: ☑ No ☐ Some recovery ☐ Mostly recovered, more sinuous ☐ Recent, severe

Canopy Cover %: ☐ Open ☑ Lightly Shaded (11-45%) ☐ Heavily Shaded ☐ Moderate Shaded (46-80%)

SEDIMENT / SUBSTRATE

Sediment Oils: ☑ Absent ☐ Slight ☐ Moderate ☐ Profuse

Sediment Odors: ☐ Normal ☐ Sewage ☐ Petroleum ☐ Chemical ☑ Anaerobic ☐ Other (Specify):

Smothering of Substrates

	None	Slight	Moderate	Severe
Sand Smothering:	☐	☐	☐	☑
Silt Smothering:	☐	☐	☑	☐
Algae Smothering:	☐	☑	☐	☐

SUBSTRATE TYPE

Assessment Tool: ☑ SCI ☑ RPS ☑ LVS ☐ LCI ☐ BioRecon

	% Coverage	INVERT # Times Sampled	PERI # Times Sampled
Woody Debris (Snags)	1.9	7	
Undercut Banks / Roots	0.5	7	
Leaf Packs or Mat			
Aquatic Vegetation			
Rock or Shell Rubble..	3	2	
Sand.....	90	2	
Mud / Muck / Silt	4	2	
Other			
Other			

WATER QUALITY

	Depth (M)	Temp. (°C)	pH (SU)	D.O. (MG/L)	D.O. Sat (%)	Cond. (UMHO/CM)	Salinity (PPT)
Top:	0.25	25.08	7.32	1.28	15.5	552.2	0.26
Mid:							
Bottom							

Secchi (M): 0.4 ☑ VOB
Total Depth: 0.4
Meter ID:

Water Odors: ☑ Normal ☐ Petroleum ☐ Sewage ☐ Chemical ☐ Other

Water Surface Oils: ☑ Normal ☐ Sheen ☐ Globs ☐ Slick ☐ Other

Water Sample Taken? ☐ Yes ☑ No
Sample Preserved? ☐ Yes ☑ No
Lot Number: Exp:

Color: ☐ Tannic ☑ Green (Algae) ☐ Clear ☐ Other (Specify)

Algae Sample Taken? ☐ Yes ☑ No
Sample Preserved? ☐ Yes ☑ No
Lot Number: Exp:

Clarity: ☐ Clear ☑ Slightly Turbid ☐ Turbid ☐ Opaque

ABUNDANCE

	Not Obs.	Rare	Common	Abundant
Periphyton:	☐	☑	☐	☐
Fish:	☐	☐	☑	☐
Aquatic Plants:	☐	☑	☐	☐
Iron/Sulfur Bacteria:	☐	☐	☑	☐

System Type: Stream ☑ Lake ☐ Wetland ☐ Estuary ☐ Other(Specify) ☐

AMBIENT FIELD CONDITIONS / NOTES:
Some water, <2m² rooted herbaceous vegetation

☑ The antecedent hydrologic conditions have been met to my best knowledge.

SAMPLING TEAM: David Eikas | **SIGNATURE:** | **DATE:** 4/30/26

Stream/River Habitat Sketch Sheet, Form FD 9000-4 (March07, 2013)
Length of grid represents 100 m of stream (not linear meters).
(Horizontal scale is double vertical scale, draw proportionately).

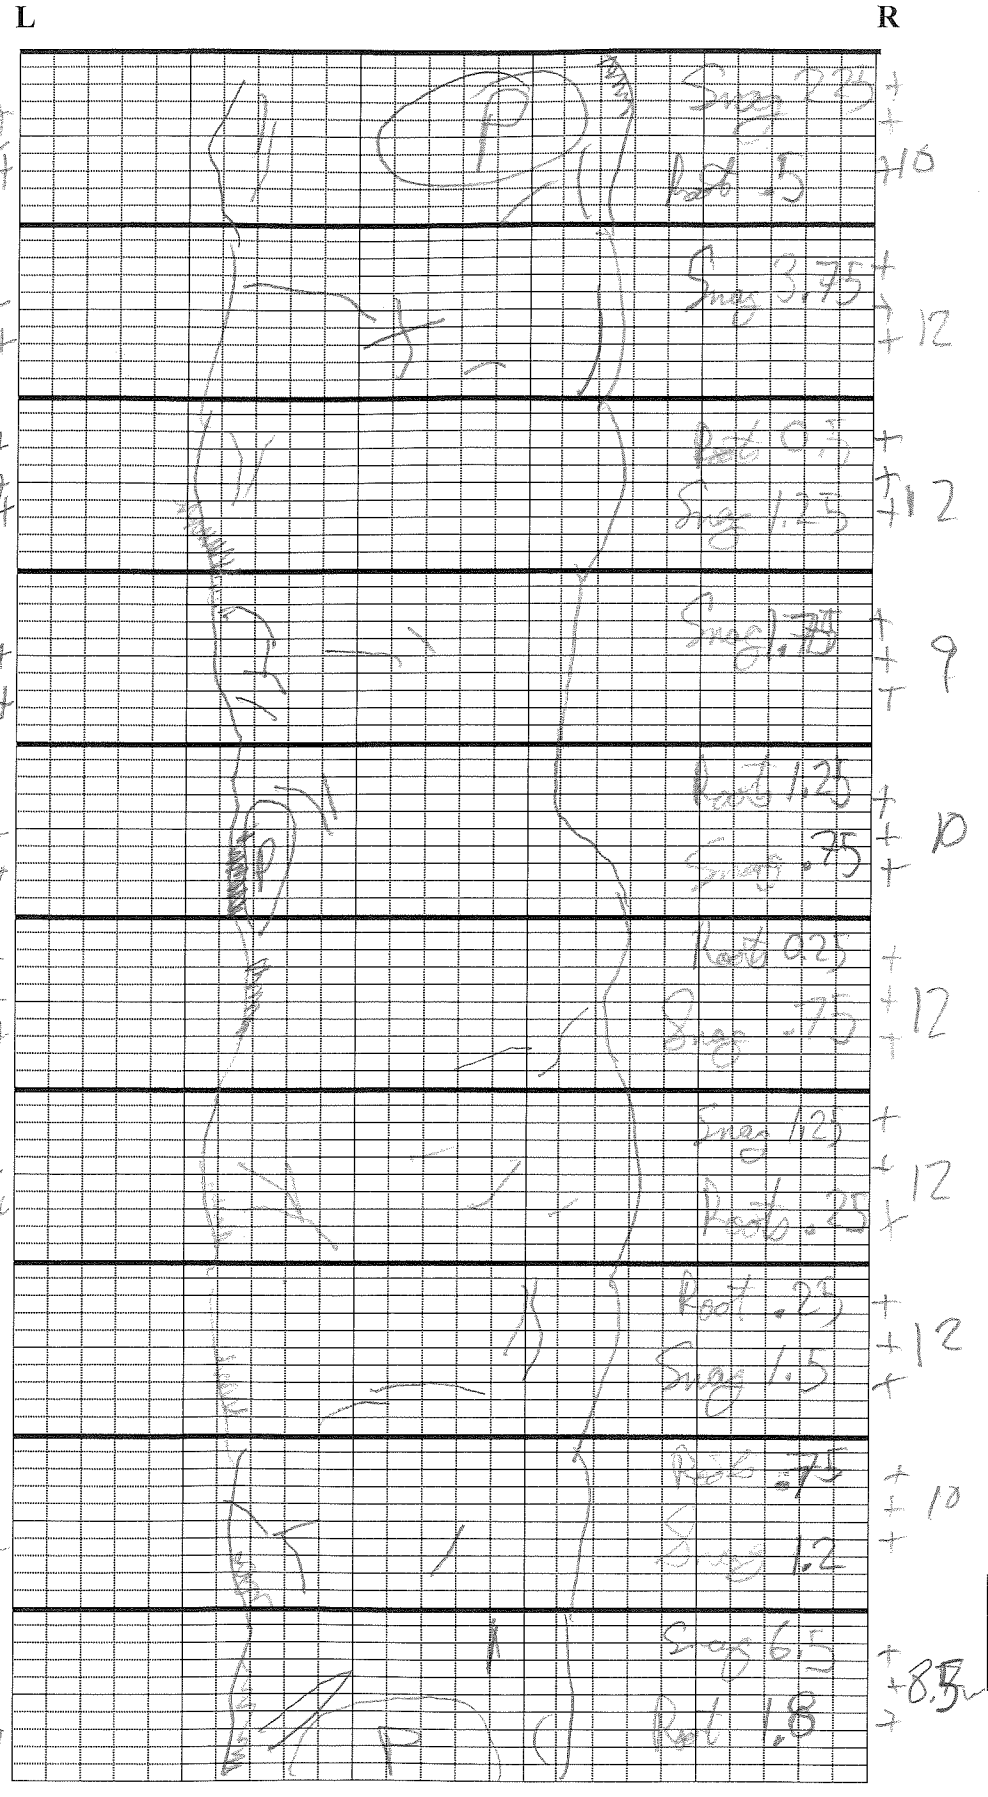

Location: Peace River Homeland
Date: 4/30/26
Samplers: [illegible]

Substrates: Code key, draw proportionate habitat abundance. %

/	Snags 20.95	1.9
\	Roots/undercut banks 5.55	0.5
9	Leaf Packs (or mats)	___
	Macrophytes	___
	_____	
	_____	

Total observed___

Pools Range expected___

Velocity measured at 60 **meter mark.** 0.08

WQ & chemistry taken at _____ **meter mark.**

Habitat Smothering:
Note areas (on map) where sand or silt is smothering substrates, limiting habitability.

Bank Stability:
Note areas (on map) with unstable, eroding banks.

Riparian Buffer Width:_____
Note areas (on map) where natural vegetation is altered or eliminated.

Plants observed/other notes:
10.75m

Prod. hab	1	2	3	4	5
Sweeps (Maj)	10	7	5	4	3
Sweeps (Min)	10	6	5	4	5

718

718

DEP Form FD 9000-5 Stream/River Habitat Assessment Field Sheet

SAMPLING AGENCY:		STORET STATION NUMBER:	DATE (MM/DD/YY):	RECEIVING BODY OF WATER:
USFWS			4/30/26	Charlotte Harbor
REMARKS:	COUNTY: Polk	LOCATION: Peace River Homeland		FIELD ID/NAME: Peace River Homeland

Habitat Parameter	Optimal	Suboptimal	Marginal	Poor
Primary Habitat Components **Substrate Diversity** 7	Four or more major productive habitats present [snags, tree roots, aquatic vegetation, leaf packs (partially decayed), rock] 20 19 18 17 16	Three major productive habitats present. Adequate habitat. Some substrates may be new fall (fresh leaves or snags) 15 14 13 12 11	Two major productive habitats present. Less than desirable habitat, frequently disturbed or removed 10 9 8 7 6	One or less major productive habitat. Lack of habitat is obvious, substrates unstable or smothered 5 4 3 2 1
Substrate Availability 3	Greater than 30% major productive habitat present at site 20 19 18 17 16	16% to 30% major productive habitat, by aerial extent 15 14 13 12 11	6% to 15% major productive habitat 10 9 8 7 6	Less than 5% major productive habitat 5 4 3 2 1
Water Velocity 8	Max. observed at typical transect: > 0.25 m/sec. But < 1 m/sec ≥0.33 0.31 0.29 0.27 >0.25 20 19 18 17 16	Max. observed at typical transect: >0.1 to 0.25 m/sec 0.25 0.21 0.17 0.13 >0.1 15 14 13 12 11	Max. observed at typical transect: 0.05 to 0.1 m/sec 0.1 0.09 0.07 0.06 0.05 10 9 8 7 6	Max. observed at typical transect: <0.05 m/sec; or spate occurring: > 1 m/sec <0.05 0.04 0.03 0.01 <0.01 5 4 3 2 1
Habitat Smothering 11 Primary Score 29	Adequate number of stable pools (1-2 per 12 times width) and <25% of habitats affected by sand, silt, or algae. 20 19 18 17 16	Adequate number of stable pools (1-2 per 12 times width) and >25% of habitats affected by sand, silt, or algae. 15 14 13 12 11	Does not have required number of stable pools (1-2 per 12 x width) and/or has shallow pools (<2 x prevailing depth). 10 9 8 7 6	Stable pools are absent. Most habitats affected by sand, silt, or algae accumulation. 5 4 3 2 1
Secondary Habitat Components **Artificial Channelization** 18	Expected sinuosity given the stream width. No evidence of dredging or artificial straightening. No spoil banks. 20 19 18 17 16	Good sinuosity within old channelized area. Evidence of dredging in the past (>25 yrs) but mostly recovered. 15 14 13 12 11	Straightened with trapezoidal cross section, but has a small degree of sinuosity developed within channelized area. 10 9 8 7 6	Straightened or engineered by dredging, has trapezoidal or box cut cross section, lacks required pools. May have spoil banks. 5 4 3 2 1
Bank Stability Right Bank 9 Left Bank 9	Bankfull > 60% of bank height. Slope of bank ≤ 60° from bankful to top of bank. Bankfull is within or above the root zone with few raw, eroded areas. 10 9	Only meets 2 of the 3 requirements for optimal bank stability. 8 7 6	Only meets 1 of the 3 requirements for optimal bank stability. 5 4	Bankfull < 60% of bank height. Slope of bank > 60°. Bankfull is below the root zone with raw, eroded areas. 3 2 1
Riparian Buffer Zone Width Right Bank 9 Left Bank 9	Width of vegetation greater than 18 m 10 9	Width of vegetation >12 to 18m 8 7 6	Width of vegetation 6 to 12 m. human activities close to system 5 4	Less than 6 m of buffer zone due to intensive human activities 3 2 1
Riparian Zone Vegetation Quality Right Bank 8 Left Bank 8 Secondary Score 70	Over 80% of riparian surfaces consist of normal, expected plant community for given sunlight & habitat conditions (e.g., native plants; tree, shrub, and forbs represented, if appropriate). Minimal disturbance. 10 9	>50% to 80% of riparian zone is undisturbed (normal, expected plant community for given sunlight & habitat conditions). Some disruption in community observed. 8 7 6	25% to 50% of riparian zone is undisturbed (normal, expected plant community for given sunlight & habitat conditions). Disruption obvious. 5 4	Less than 25% of riparian zone is undisturbed (normal, expected plant community for given sunlight & habitat conditions). 3 2 1

99 **TOTAL SCORE**

Date: 4/30/26	Analyst: David Eilers	Signature:

DEP FORM FD 9000-25 Rapid Periphyton Survey Field Sheet

Site: Peace River Homestead | County: Polk | Date: 4/30/26 | Investigators: DEilers

STORET Station Number:

Transect (m)	Point 1=right 9=left	Algal Thickness Rank (N-6, X)	Estimated	Canopy Cover	Transect (m)	Point 1=right 9=left	Algal Thickness Rank (N-6, X)	Estimated	Canopy Cover
0	1	N			60	1	N		
	2	N				2	3		
	3	N				3	N		
	4	N				4	N		
	5	N		21		5	N		20
	6	N				6	N		
	7	N				7	N		
	8	N				8	N		
	9	N				9	N		
10	1	N			70	1	N		
	2	N				2	N		
	3	N				3	N		
	4	N				4	N		
	5	N		15		5	N		13
	6	N				6	N		
	7	N				7	N		
	8	N				8	N		
	9	N				9	N		
20	1	3			80	1	3		
	2	N				2	N		
	3	N				3	N		
	4	N				4	N		
	5	N		12		5	N		26
	6	N				6	N		
	7	N				7	N		
	8	3				8	N		
	9	N				9	N		
30	1	N			90	1	N		
	2	N				2	N		
	3	N				3	N		
	4	N				4	N		
	5	N		8		5	N		0
	6	N				6	N		
	7	N				7	N		
	8	N				8	N		
	9	N				9	N		
40	1	N			100	1	N		
	2	3				2	N		
	3	N				3	N		
	4	N				4	N		
	5	N		8		5	3		0
	6	N				6	N		
	7	N				7	N		
	8	N				8	N		
	9	N				9	N		
50	1	N							
	2	N							
	3	N							
	4	N							
	5	N		25					
	6	N							
	7	N							
	8	3							
	9	3							

Secchi depth	1.4
Estimated?	✓

# points ranked 4-6	0
total points assessed	99
% points ranked 4-6	0

Check accompanying data collected at same site/date.	
Algal mat sample	
Linear Veg Survey	
Habitat Assessment	✓
SCI/Bioreconn	✓
Water sample	

RQ-

Algal Thickness Rank	
N	rough, no algae, slimy, algae up to 1mm
3	>1mm - 6mm
4	>6mm - 20mm
5	>20mm - 10 cm
6	>10 cm

Record "N" and check "Estimated" for points deeper than the Secchi depth; algae are presumed absent. Check "Estimated" if thickness estimated for deep points which can be seen but not reached.

Record "X" for points shallower than Secchi depth for which substrate cannot be seen or reached with the hand. No estimated rank.

Record canopy cover as the number of small densiometer quadrants (out of 96) that HAVE canopy cover. Measure facing upstream at point 4, 5, or 6.

Collect algal mat sample following DEP SOP FS 7240 if the percentage of total sampled points with a thickness rank of 4, 5, or 6 is >20%.
